



ENTERPRISE
information services

Statewide Parcels Update

Melissa Foltz

Spring Framework Forum

May 15, 2025





Thank You to the Participating Counties!

- ▶ Baker
- ▶ Harney
- ▶ Marion
- ▶ Washington
- ▶ Yamhill





Project History (2023-2024)

- ▶ Determined Data Scheme
- ▶ Developed Data Validation Rules and Processes
- ▶ Data Intake / QAQC / Testing
- ▶ Scripting for Transformation and Archiving
- ▶ Compiled a Draft Web Viewer
- ▶ Worked on Onboarding/Training Materials





Project History (2025)


- ▶ Unable to pass testing
- ▶ Staff transitions
- ▶ Unable to scale






Today

- ▶ Reassess the need
- ▶ Revisit our goals
- ▶ Simplify the product

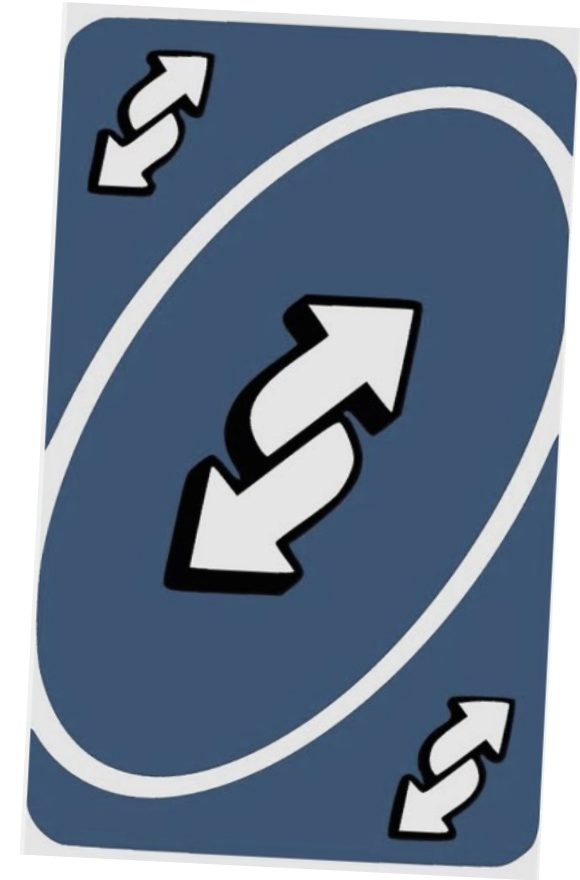

Expectation

Consolidated Web Viewer

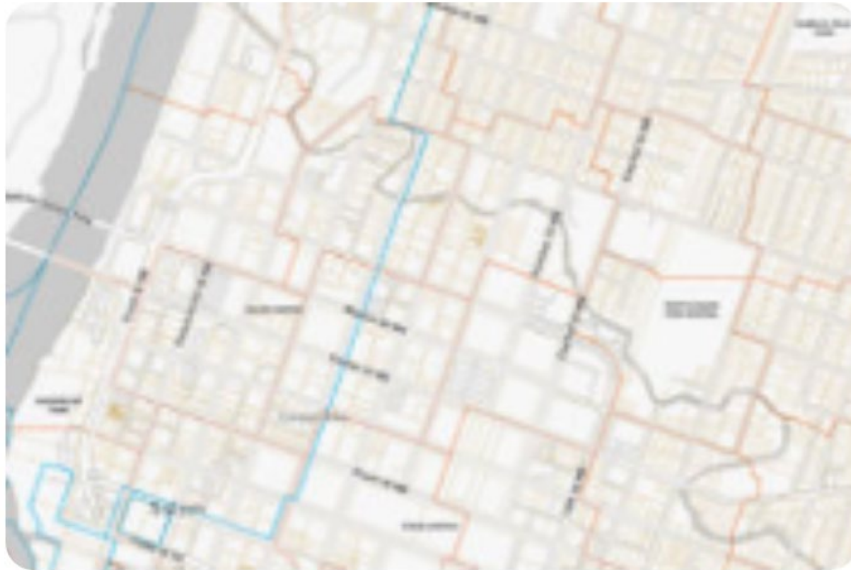

Oregon Parcel Database

✓ Authoritative



OR FRAMEWORK
State of Oregon

Reality

Collection of Web Viewers





Lessons Learned

- ▶ No Primary Use Case was identified
- ▶ Were not able to scale the effort without automated workflows
- ▶ Need a better understanding of existing efforts
- ▶ Outstanding concerns regarding data quality





Moving Forward

- ▶ Continue working with OGIC
- ▶ Focus on data governance and data sharing
- ▶ Focus on aligning/leveraging existing efforts rather than duplicating efforts





ENTERPRISE
information services

Thank You

Melissa.foltz@das.Oregon.gov

